


Jack R. Meredith
Samuel J. Mantel, Jr.

PROJECT MANAGEMENT

A MANAGERIAL APPROACH

Fourth Edition

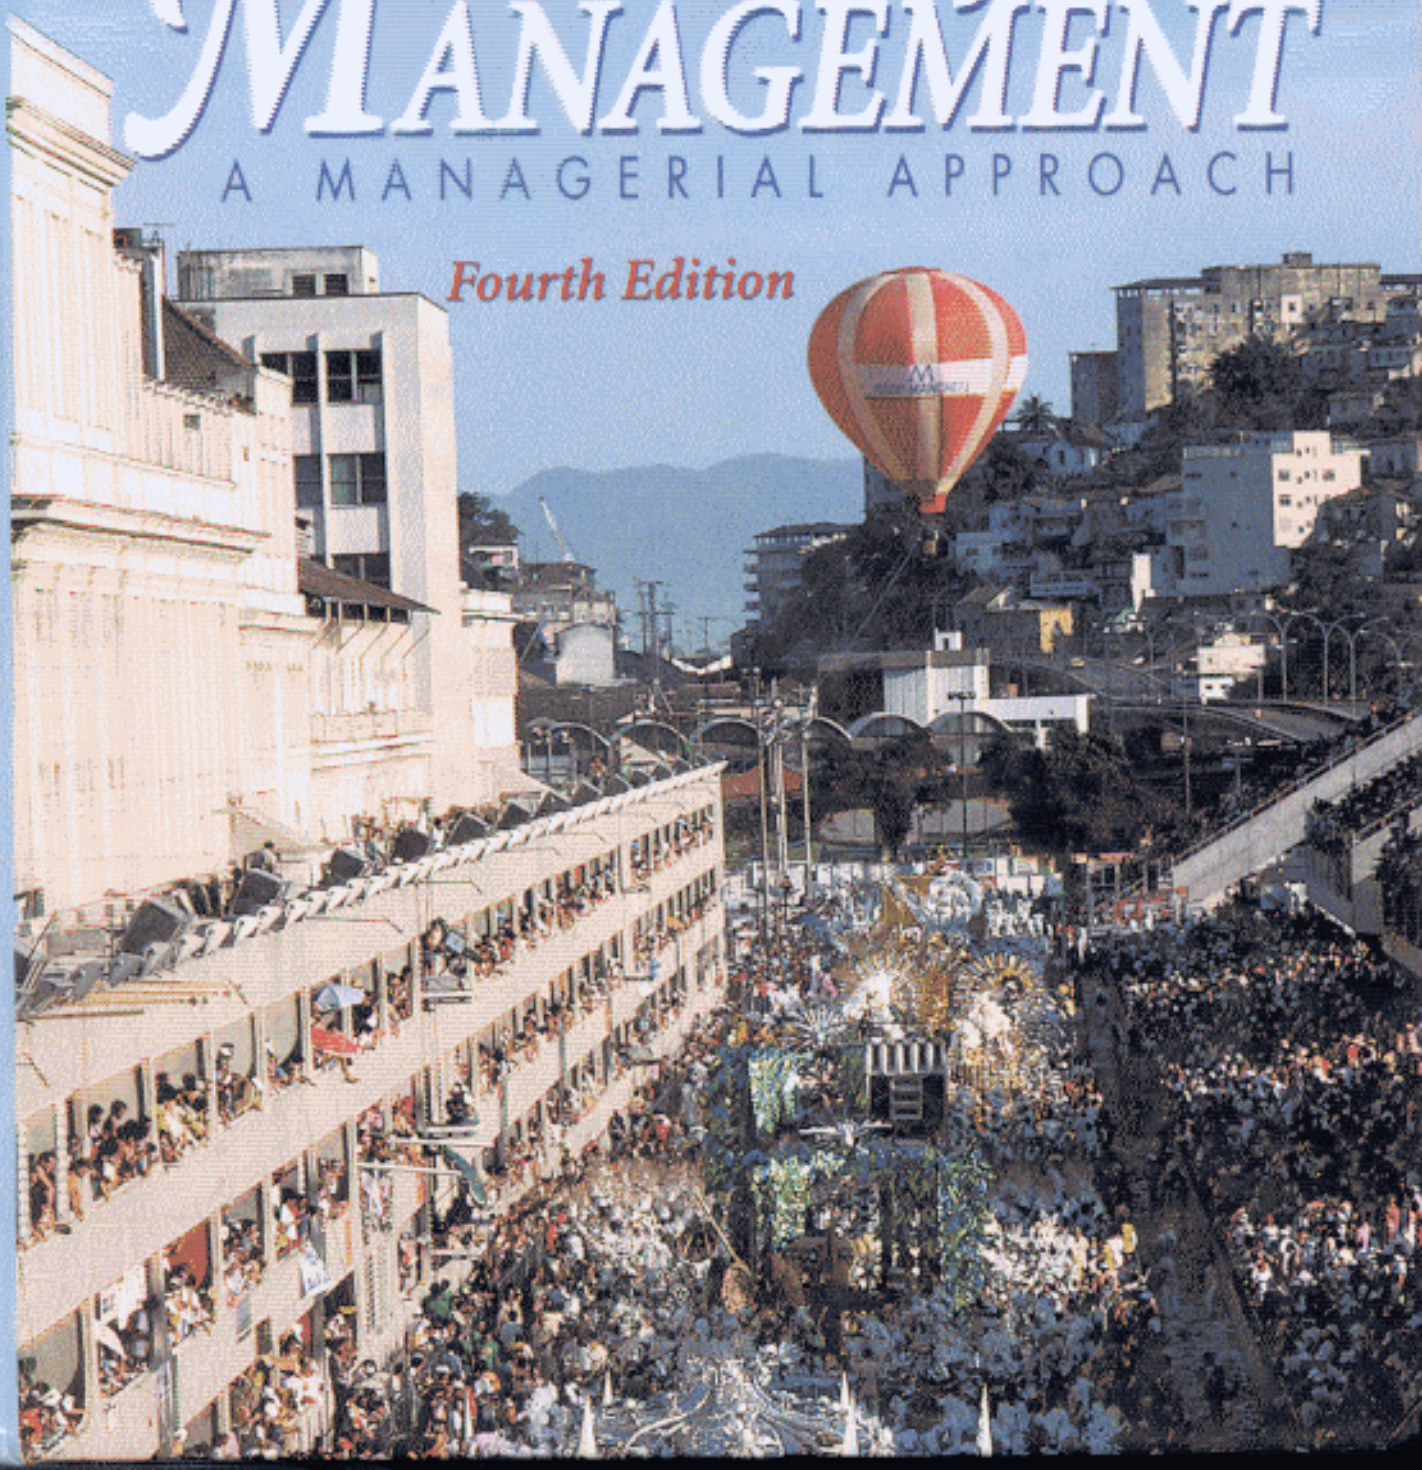

Contents

1 Projects in Contemporary Organizations, 1

- 1.1 The Definition of a "Project", 8
- 1.2 Why Project Management?, 12
- 1.3 The Project Life Cycle, 14
- 1.4 The Structure of This Text, 19
 - PROJECT MANAGEMENT IN PRACTICE: Implementing Strategy Through Projects at Blue Cross/Blue Shield, 8
 - PROJECT MANAGEMENT IN PRACTICE: The Olympic Torch Relay Project, 11
 - PROJECT MANAGEMENT IN PRACTICE: Demolishing San Francisco's Bridges Safely, 18
 - DIRECTED READING: Lessons for an Accidental Profession, 25

PART I PROJECT INITIATION

2 Project Selection, 39

- 2.1 Criteria for Project Selection Models, 40
- 2.2 The Nature of Project Selection Models, 42
- 2.3 Types of Project Selection Models, 45
- 2.4 Analysis Under Uncertainty—The Management of Risk, 62
- 2.5 Comments on the Information Base for Selection, 66
- 2.6 Project Proposals, 68
 - PROJECT MANAGEMENT IN PRACTICE: Project Selection for Spent Nuclear Fuel Cleanup, 52
 - PROJECT MANAGEMENT IN PRACTICE: Selecting a Composting Project at Larry's Markets, 61

PROJECT MANAGEMENT IN PRACTICE: The Military Mobile Communication System—A Procurement Innovation, 71

DIRECTED READING: Automotive Builders, Inc.: The Stanhope Project, 79

3 The Project Manager, 85

- 3.1 Project Management and the Project Manager, 87
- 3.2 Special Demands on the Project Manager, 95
- 3.3 Selecting the Project Manager, 107
- 3.4 Problems of Cultural Differences, 112
- 3.5 Impact of Institutional Environments, 117
- 3.6 Multicultural Communications and Managerial Behavior, 124
 - PROJECT MANAGEMENT IN PRACTICE: The Project Management Career Path at AT&T, 93
 - PROJECT MANAGEMENT IN PRACTICE: The Wreckmaster at a New York Subway Accident, 104
 - PROJECT MANAGEMENT IN PRACTICE: Success at Energo by Integrating Two Diverse Cultures, 116
 - PROJECT MANAGEMENT IN PRACTICE: Project Management in Brazil During Unstable Times, 121
 - DIRECTED READING: What It Takes to Be A Good Project Manager, 134

4 Project Organization, 139

- 4.1 The Project as Part of the Functional Organization, 141
- 4.2 Pure Project Organization, 145

- 4.3 The Matrix Organization, 147
- 4.4 Mixed Organizational Systems, 152
- 4.5 Choosing an Organizational Form, 154
- 4.6 The Project Team, 160
- 4.7 Human Factors and the Project Team, 163

PROJECT MANAGEMENT IN PRACTICE:
Reorganizing for Project Management at
Prevost Car, 144

PROJECT MANAGEMENT IN PRACTICE:
Converting to Project Management in
Government Agencies, 159

PROJECT MANAGEMENT IN PRACTICE:
South African Repair Success through
Teamwork, 168

DIRECTED READING: The Virtual Project:
Managing Tomorrow's Team Today, 175

5 Project Planning, 182

- 5.1 Initial Project Coordination, 184
- 5.2 Systems Integration, 192
- 5.3 Sorting Out the Project, 193
- 5.4 The Work Breakdown Structure and Linear Responsibility Charts, 203
- 5.5 Interface Coordination through Integration Management, 209
 - PROJECT MANAGEMENT IN PRACTICE:
Extensive Project Planning for Kodak's New Photographic System, 190
 - PROJECT MANAGEMENT IN PRACTICE:
Disaster Project Planning in Iceland, 202
 - DIRECTED READING: Planning for Crisis in Project Management, 217

6 Conflict and Negotiation, 226

- 6.1 The Nature of Negotiation, 229
- 6.2 Partnering, Chartering, and Change, 230
- 6.3 Conflict and the Project Life Cycle, 234
- 6.4 Some Requirements and Principles of Negotiation, 243
- 6.5 Negotiation in Action—The Quad Sensor Project, 246
 - PROJECT MANAGEMENT IN PRACTICE: Selling New Area Codes to Consumers Who Don't Want Them, 228

PROJECT MANAGEMENT IN PRACTICE:
A Consensus Feasibility Study for
Montreal's Archipel Dam, 242
DIRECTED READING: Methods of Resolving In-
terpersonal Conflict, 252

PART II PROJECT IMPLEMENTATION

7 Budgeting and Cost Estimation, 261

- 7.1 Estimating Project Budgets, 264
- 7.2 Improving the Process of Cost Estimation, 276
 - PROJECT MANAGEMENT IN PRACTICE: Pathfinder Mission to Mars—on a Shoestring, 263
 - PROJECT MANAGEMENT IN PRACTICE:
Completing the Limerick Nuclear Facility Under Budget, 274
 - PROJECT MANAGEMENT IN PRACTICE: Managing Costs at Massachusetts' Neighborhood Health Plan, 290
 - DIRECTED READING: Three Perceptions of Project Cost, 295

8 Scheduling, 302

- 8.1 Background, 302
- 8.2 Network Techniques: PERT and CPM, 307
- 8.3 Gantt Charts, 332
- 8.4 Extensions and Applications, 339
 - PROJECT MANAGEMENT IN PRACTICE: Replacing the Atigun Section of the Trans Alaska Pipeline, 304
 - PROJECT MANAGEMENT IN PRACTICE: Hosting the Annual Project Management Institute Symposium, 336
 - DIRECTED READING: The Sharon Construction Corporation, 359

9 Resource Allocation, 361

- 9.1 Critical Path Method—Crashing a Project, 363
- 9.2 The Resource Allocation Problem, 371
- 9.3 Resource Loading, 372
- 9.4 Resource Leveling, 375

- 9.5 Constrained Resource Scheduling, 378
- 9.6 Multiproject Scheduling and Resource Allocation, 388
- PROJECT MANAGEMENT IN PRACTICE: Expediting Los Angeles Freeway Repairs After the Earthquake, 362
- PROJECT MANAGEMENT IN PRACTICE: Benefits of Resource Constraining at Pennsylvania Electric, 387
- PROJECT MANAGEMENT IN PRACTICE: Minnesota DOT Ties Projects to Resources and Constraints, 399
- DIRECTED READING: D. U. Singer Hospital Products Corp., 407

10 Monitoring and Information Systems, 410

- 10.1 The Planning-Monitoring-Controlling Cycle, 412
- 10.2 Information Needs and the Reporting Process, 422
- 10.3 Computerized PMIS (Project Management Information Systems), 437
- PROJECT MANAGEMENT IN PRACTICE: Using Project Management Software to Schedule the Olympic Games, 411
- PROJECT MANAGEMENT IN PRACTICE: Tracking Scope Creep: A Project Manager Responds, 421
- PROJECT MANAGEMENT IN PRACTICE: Success Through Earned Value at Texas Instruments, 433
- DIRECTED READING: Survey of Project Management Tools, 453

11 Project Control, 462

- 11.1 The Fundamental Purposes of Control, 464
- 11.2 Three Types of Control Processes, 468
- 11.3 Comments on the Design of Control Systems, 476
- 11.4 Control as a Function of Management, 482
- 11.5 Balance in a Control System, 487
- 11.6 Control of Creative Activities, 490
- 11.7 Control of Change and Scope Creep, 491

- PROJECT MANAGEMENT IN PRACTICE: Extensive Controls for San Francisco's Metro Turnback Project, 466
- PROJECT MANAGEMENT IN PRACTICE: Schedule and Cost Control for Australia's New Parliament House, 483
- PROJECT MANAGEMENT IN PRACTICE: Better Control of Development Projects at Johnson Controls, 494
- DIRECTED READING: Controlling Projects According to Plan, 500

PART III PROJECT TERMINATION

12 Project Auditing, 511

- 12.1 Purposes of Evaluation—Goals of the System, 512
- 12.2 The Project Audit, 515
- 12.3 Construction and Use of the Audit Report, 519
- 12.4 The Project Audit Life Cycle, 523
- 12.5 Some Essentials of an Audit/Evaluation, 525
- 12.6 Measurement, 528
- PROJECT MANAGEMENT IN PRACTICE: Lessons from Auditing 110 Client/Server and Open Systems Projects, 515
- PROJECT MANAGEMENT IN PRACTICE: Auditing a Troubled Project at Atlantic States Chemical Laboratories, 522
- DIRECTED READING: Post-Project Appraisals Pay, 534

13 Project Termination, 539

- 13.1 The Varieties of Project Termination, 540
- 13.2 When to Terminate a Project, 545
- 13.3 The Termination Process, 551
- 13.4 The Final Report—A Project History, 557
- PROJECT MANAGEMENT IN PRACTICE: Nucor's Approach to Termination by Addition, 542
- PROJECT MANAGEMENT IN PRACTICE: Terminating the Superconducting Super Collider Project, 550

DIRECTED READING: Knowing When to Pull
the Plug, 563

Epilogue, 571

On the Need for a Universal Information
System, 572

On the Need for Conflict Resolution in
Matrix Management, 573

On the Need for New Methods of
Rewarding Excellence, 574

**Appendix A: Area Under the Normal
Distribution, 575**

Appendix B: Probability and Statistics, 577

B.1 Probability, 577

B.2 Event Relationships and Probability
Laws, 578

B.3 Statistics, 581

**Appendix C: Answers to the Even-Numbered
Problems, 588**

Photo Credits, 593

Author Index, 595

Subject Index, 605
