


INFORMATION TECHNOLOGY PROJECT MANAGEMENT

Providing Measurable Organizational Value



JACK T. MARCHEWKA

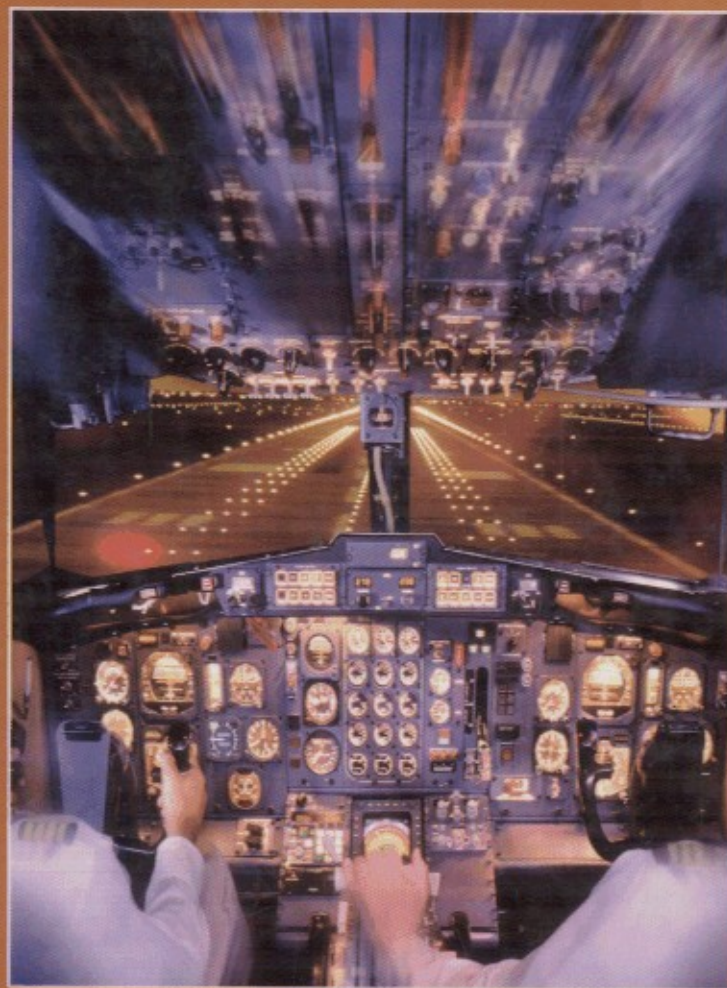

CONTENTS

PREFACE xv

ABOUT THE AUTHOR xxi

CHAPTER 1	The Nature of Information Technology Projects	1
	Global Technology Solutions	1
	Introduction	2
	How This Book Is Organized	3
	The Software Crisis	4
	Why IT Projects Fail	4
	Improving the Likelihood of Success	6
	<i>A Socio-Technical Approach</i>	6
	<i>A Project-Management Approach</i>	7
	<i>A Knowledge-Management Approach</i>	8
	The Context of Project Management	9
	What Is a Project?	9
	<i>Attributes of a Project</i>	9
	The Project Life Cycle and IT Development	12
	Define Project Goal	12
	Plan Project	13
	Execute Project Plan	13
	Close Project	14
	Evaluate Project	14
	The IT Product Life Cycle	14
	<i>Planning</i>	15
	<i>Analysis</i>	15
	<i>Design</i>	15
	<i>Implementation</i>	15
	<i>Maintenance and Support</i>	15
	Putting the SDLC into Practice	16

<i>Structured Approach to Systems Development</i>	16
<i>Rapid Applications Development (RAD)</i>	16
The PLC versus the SDLC	18
The Project Management Body of Knowledge (PMBOK)	19
Project Management Knowledge Areas	19
<i>Chapter Summary</i>	21
<i>Review Questions</i>	21
<i>Extend Your Knowledge</i>	22
<i>Bibliography</i>	22

CHAPTER 2 Conceptualizing and Initializing the IT Project 23

Global Technology Solutions	23
Introduction	25
An Information Technology Project Methodology (ITPM)	25
Phase 1: Conceptualize and Initialize	27
Phase 2: Develop the Project Charter and Detailed Project Plan	28
Phase 3: Execute and Control the Project	29
Phase 4: Close Project	29
Phase 5: Evaluate Project Success	30
IT Project Management Foundation	30
<i>Project Management Processes</i>	31
<i>Project Objectives</i>	31
<i>Tools</i>	31
<i>Infrastructure</i>	31
<i>Project Management Knowledge Areas</i>	32
The Business Case	32
What Is a Business Case?	32
Developing the Business Case	33
<i>Step 1: Select the Core Team</i>	33
<i>Step 2: Define Measurable Organizational Value (MOV)</i>	34
<i>Step 3: Identify Alternatives</i>	40
<i>Step 4: Define Feasibility and Assess Risk</i>	41
<i>Step 5: Define Total Cost of Ownership</i>	42
<i>Step 6: Define Total Benefits of Ownership</i>	42
<i>Step 7: Analyze Alternatives</i>	43
<i>Step 8: Propose and Support the Recommendation</i>	47
Project Selection and Approval	48
The IT Project Selection Process	49
The Project Selection Decision	49

<i>Chapter Summary</i>	52
<i>Review Questions</i>	53
<i>Extend Your Knowledge</i>	54
<i>Bibliography</i>	54

CHAPTER 3 Developing the Project Charter and Baseline Project Plan 55

Global Technology Solutions	55
Introduction	56
Project Management Processes	57
Project Management Process Groups	58
<i>Initiating</i>	58
<i>Planning</i>	59
<i>Executing</i>	60
<i>Controlling</i>	60
<i>Closing</i>	60
Project Integration Management	60
Project Plan Development	61
Project Plan Execution	62
Overall Change Control	62
The Project Charter	63
What Should Be in a Project Charter?	65
<i>Project Identification</i>	65
<i>Project Stakeholders</i>	65
<i>Project Description</i>	65
<i>Measurable Organizational Value (MOV)</i>	65
<i>Project Scope</i>	65
<i>Project Schedule</i>	66
<i>Project Budget</i>	66
<i>Quality Issues</i>	66
<i>Resources</i>	66
<i>Assumptions and Risks</i>	66
<i>Project Administration</i>	67
<i>Acceptance and Approval</i>	67
<i>References</i>	67
<i>Terminology</i>	67
Project Planning Framework	68
The MOV	69
Define the Project's Scope	69
Subdivide the Project into Phases	70
Tasks—Sequence, Resources, and Time Estimates	70

Sequence 70
Resources 70
Time 71
Schedule and Budget—The Baseline Plan 71
The Kick-Off Meeting 71
Chapter Summary 72
Review Questions 72
Extend Your Knowledge 73

CHAPTER 4 The Human Side of Project Management 74

Global Technology Solutions 74
Introduction 75
Organization and Project Planning 76
 The Formal Organization 77
 The Functional Organization 77
 The Project Organization 81
 The Matrix Organization 82
 Which Organizational Structure Is Best? 84
 The Informal Organization 85
 Stakeholders 85
 Stakeholder Analysis 85
The Project Team 86
 The Roles of the Project Manager 86
 Team Selection and Acquisition 88
 Team Performance 88
 Work Groups 89
 Real Teams 89
 Project Teams and Knowledge Management 91
 Learning Cycles and Lessons Learned 92
The Project Environment 96
 Chapter Summary 97
 Review Questions 98
 Extend Your Knowledge 99
 Bibliography 100

CHAPTER 5 Defining and Managing Project Scope 101

Global Technology Solutions 101
Introduction 102
 Project Scope Management Processes 102

Project Scope Initiation	104
Project Scope Planning	105
Scope Boundary	105
The Scope Statement	105
<i>Scope Statement</i>	105
<i>Out of Scope for this Project</i>	106
Project Scope Definition	107
Project-Oriented Scope	107
<i>Project-Oriented Scope Definition Tools</i>	107
Product-Oriented Scope	109
<i>Product-Oriented Scope Definition Tools</i>	109
Project Scope Verification	111
Scope Change Control	113
Scope Change Control Procedures	114
Benefits of Scope Control	117
<i>Chapter Summary</i>	117
<i>Review Questions</i>	117
<i>Extend Your Knowledge</i>	119
<i>Bibliography</i>	119

CHAPTER 6 The Work Breakdown Structure and Project Estimation 120

Global Technology Solutions	120
Introduction	122
The Work Breakdown Structure (WBS)	123
Work Packages	123
Deliverables and Milestones	124
Developing the WBS	125
<i>The WBS Should Be Deliverable-Oriented</i>	126
<i>The WBS Should Support the Project's MOV</i>	126
<i>The Level of Detail Should Support Planning and Control</i>	127
<i>Developing the WBS Should Involve the People Who Will Be Doing the Work</i>	128
<i>Learning Cycles and Lessons Learned Can Support the Development of a WBS</i>	128
Project Estimation	128
Guesstimating	128
Delphi Technique	129
Time Boxing	129
Top-Down Estimating	129
Bottom-Up Estimating	130

- Software Engineering Metrics and Approaches 131
 - Lines of Code (LOC) 133
 - Function Points 133
 - COCOMO 137
 - Heuristics 139
 - Automated Estimating Tools 140
- What Is the Best Way to Estimate IT Projects? 140
 - Chapter Summary 141
 - Web Sites to Visit 142
 - Review Questions 142
 - Extend Your Knowledge 143
 - Bibliography 144

CHAPTER 7 The Project Schedule and Budget 146

- Global Technology Solutions 146
- Introduction 148
- Developing the Project Schedule 149
 - Gantt Charts 150
 - Project Network Diagrams 150
 - Activity on the Node (AON) 151
 - Critical Path Analysis 152
 - PERT 153
 - Precedence Diagramming Method (PDM) 154
- Project Management Software Tools 156
- Developing the Project Budget 158
 - Cost Estimation 159
 - Other Costs 161
 - Resource Allocation 163
- Finalizing the Project Schedule and Budget 163
 - Chapter Summary 164
 - Review Questions 165
 - Extend Your Knowledge 165
 - Bibliography 165

CHAPTER 8 Managing Project Risk 166

- Global Technology Solutions 166
- Introduction 168
- IT Project Risk Management Planning Process 170
 - Risk Planning 171

Risk Identification	171
Risk Assessment	172
Risk Strategies	172
Risk Monitoring and Control	173
Risk Response	173
Risk Evaluation	173
Identifying IT Project Risks	173
An IT Project Risk Management Framework	174
Applying the IT Project Risk Management Framework	175
Tools and Techniques	177
Risk Analysis and Assessment	179
Qualitative Approaches	179
<i>Expected Value</i>	180
<i>Decision Trees</i>	180
<i>Risk Impact Table</i>	181
Quantitative Approaches	183
<i>Discrete Probability Distributions</i>	183
<i>Continuous Probability Distributions</i>	184
<i>Simulations</i>	187
Risk Strategies	190
Risk Monitoring and Control	192
Risk Response and Evaluation	193
<i>Chapter Summary</i>	194
<i>Web Sites to Visit</i>	195
<i>Review Questions</i>	195
<i>Extend Your Knowledge</i>	196
<i>Bibliography</i>	196

CHAPTER 9 Project Communication, Tracking, and Reporting 197

Global Technology Solutions	197
Introduction	199
Monitoring and Controlling the Project	200
The Project Communications Plan	202
Project Metrics	203
Earned Value	205
Reporting Performance and Progress	209
Information Distribution	210
<i>Chapter Summary</i>	213
<i>Review Questions</i>	215

Extend Your Knowledge 216

Bibliography 216

CHAPTER 10 IT Project Quality Management 217

Global Technology Solutions 217

Introduction 220

The Quality Movement 223

Craftsmanship 223

The Industrial Revolution 224

Frederic W. Taylor (1856–1915) 224

Walter A. Shewhart (1891–1967) 225

W. Edwards Deming (1900–1993) 227

Joseph Juran (1904–) 228

Kaoru Ishikawa (1915–) 229

Phillip Crosby (1926–2001) 231

Quality Systems 231

International Organization for Standardization (ISO) 231

TickIT 234

Six Sigma (6σ) 234

The Capability Maturity Model (CMM) 236

Level 1: Initial 237

Level 2: Repeatable 238

Level 3: Defined 239

Level 4: Managed 239

Level 5: Optimizing 240

The IT Project Quality Plan 241

Quality Philosophies and Principles 241

Focus on Customer Satisfaction 242

Prevention not Inspection 242

Improve the Process to Improve the Product 243

Quality Is Everyone's Responsibility 243

Fact-Based Management 243

Quality Standards and Metrics 243

Verification and Validation 245

Change Control and Configuration Management 247

Component Identification 248

Version Control 248

Configuration Building 248

Change Control 249

Monitor and Control 249
 Learn, Mature, and Improve 249

Chapter Summary 250
Web Sites to Visit 252
Review Questions 252
Extend Your Knowledge 253
Bibliography 253

CHAPTER 11 Managing Organizational Change, Resistance, and Conflict 256

Global Technology Solutions 256
Introduction 258

The Nature of Change 260
 The Impact of Change 260
 Change as a Process 262
 Emotional Responses to Change 263

The Change Management Plan 264

Assess Willingness, Readiness, and Ability to Change 264
Sponsor 264
Change Agents 265
Targets 265

Develop or Adopt a Strategy for Change 266

Rational-Empirical Approach 267
Normative-Reeducation Approach 267
Power-Coercive Approach 268
Environmental-Adaptive Approach 269

Implement the Change Management Plan and Track Progress 270

Evaluate Experience and Develop Lessons Learned 270

Dealing with Resistance and Conflict 270

Resistance 270
 Conflict 271
 Polarity Management 274

Chapter Summary 277
Review Questions 278
Extend Your Knowledge 279
Bibliography 280

CHAPTER 12 Project Implementation, Closure, and Evaluation 281

Global Technology Solutions 281

Introduction	282
Project Implementation	283
Direct Cutover	284
Parallel	285
Phased	285
Administrative Closure	287
Project Sponsor Acceptance	289
The Final Project Report	290
The Final Meeting and Presentation	291
Closing the Project	291
Project Evaluation	292
Individual Performance Review	292
Postmortem Review	293
Project Audit	294
Evaluating Project Success—The MOV	295
<i>Chapter Summary</i>	296
<i>Review Questions</i>	297
<i>Extend Your Knowledge</i>	297
<i>Bibliography</i>	298

APPENDIX A: An Introduction to Function Point Analysis	301
---	-----

INDEX	315
--------------	-----
