


GREEN CONSTRUCTION PROJECT MANAGEMENT AND COST OVERSIGHT



SAM KUBBA
Ph.D., LEED AP

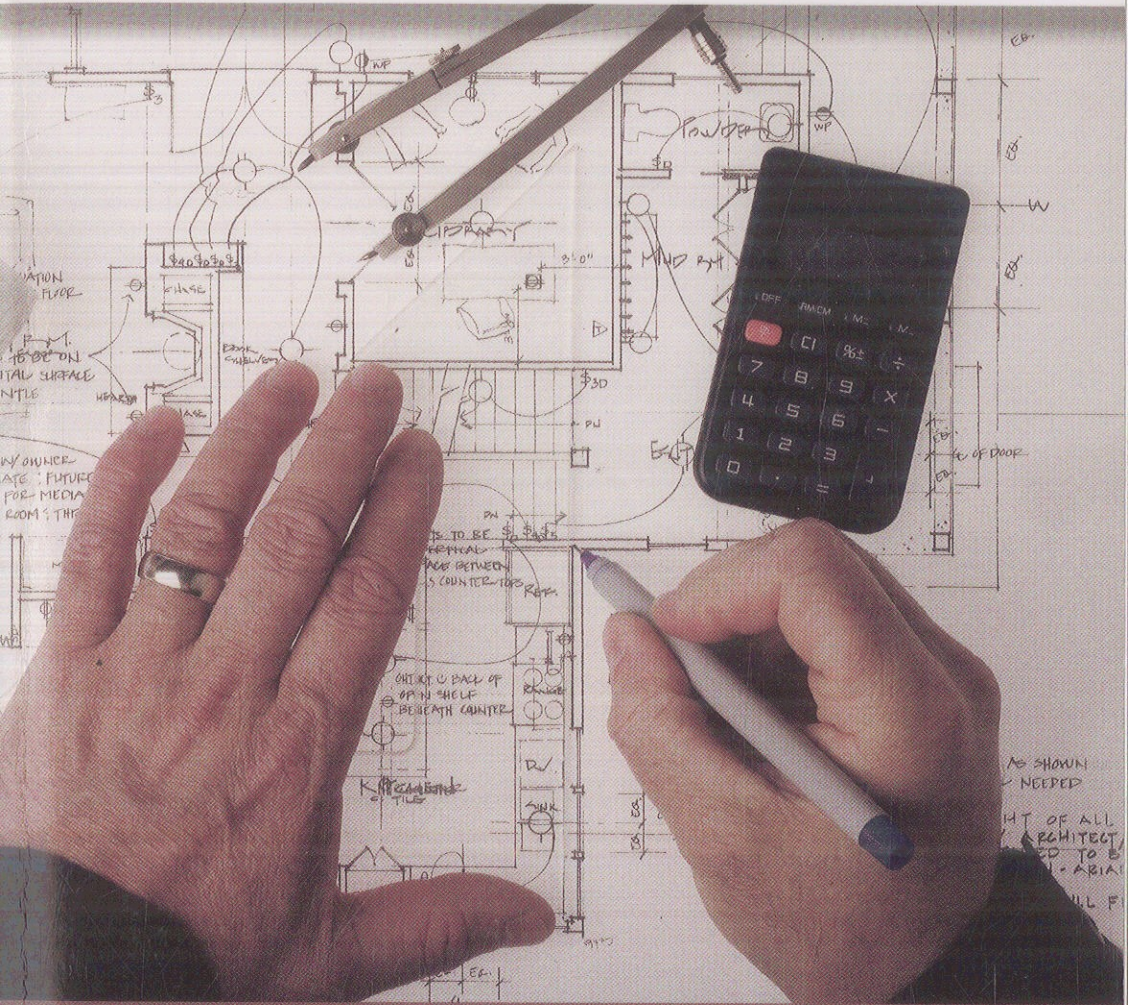

Contents

Foreword xi

Acknowledgments xiii

Introduction xv

1

“GREEN” AND “SUSTAINABILITY” DEFINED

- 1.1 General—Overview of the Green Building Movement 1
- 1.2 What is Green Design? Basic Green Concepts 4
 - 1.3 Establishing Measurable Green Criteria 7
- 1.4 Benefits of Going Green—Incentives and Barriers 13
- 1.5 Emerging Directions—A Recent Upsurge in Green Building 17

2

ELEMENTS OF GREEN DESIGN AND CONSTRUCTION

- 2.1 General 28
- 2.2 Green Rating Standards Used Worldwide 31
- 2.3 LEED™ Certification and Rating System 45
 - 2.4 The Green Globes™ Rating System 54

3

GREEN PROJECT REQUIREMENTS AND STRATEGIES

- 3.1 General 72
- 3.2 Green Building Principals and Components 76
- 3.3 Identifying Green Project Requirements and Strategies 89
- 3.4 Design Process for High Performance Buildings 96
 - 3.5 Green Project Delivery Systems 100
- 3.6 Traditional Green Design-Bid-Build Project Delivery 101
 - 3.7 Green Construction Management 103
 - 3.8 Green Design-Build Project Delivery 106

4

GREEN CONSTRUCTION COST MONITORING

- 4.1 General 113
- 4.2 Front-end Analysis 114
- 4.3 Requisition Format 116
- 4.4 Site Visits and Observations 122
- 4.5 Loan Disbursements—Draw Application Reviews 132
- 4.6 Preparing the Progress Status Report (PSR) 143
- 4.7 Final Certification and Project Closeout 153
- 4.8 Quality Control/Quality Assurance 165

5

HOW THE CONSULTANT FUNCTIONS IN THE REQUISITION PROCESS

- 5.1 General 169
- 5.2 Areas of Concern to the Lender and Borrower 173
- 5.3 Owner Needs and Expectations 180
- 5.4 Confidentiality of Reports and Documents 185
- 5.5 Typical Sequence of Events Upon Being Awarded a Project Assignment 187
- 5.6 The Consultant's Responsibilities and Qualifications 197
- 5.7 Avoiding Conflicts of Interest 204
- 5.8 Typical Agreements 205
- Section 1: Consultant Services 206
- Section 2: General 212

6

CHOOSING MATERIALS AND PRODUCTS

- 6.1 General 222
- 6.2 Low Emitting Materials 226
- 6.3 Building and Material Reuse and Recyclable Materials 250
- 6.4 Construction Waste Management 254
- 6.5 Regional Materials 254
- 6.6 Certified Forestry Products and Rapidly Renewable Materials 255
- 6.7 Green Office Equipment 262
- 6.8 Life-Cycle Assessment of Building Materials and Products 264

7

PROJECT COST BREAKDOWN

- 7.1 General 267
- 7.2 Budget Development—An Analysis 271
- 7.3 Buyouts 278
- 7.4 General Conditions and Supplemental Conditions 285
- 7.5 Contingencies and Allowances 290
- 7.6 Project Cost Management 296

8

GREEN DESIGN AND CONSTRUCTION ECONOMICS

- 8.1 General 305
- 8.2 The Economics of Green Design—Costs and Benefits 308
- 8.3 Life Cycle Costing (LCC) 325
- 8.4 Tax Benefits 330
- 8.5 Miscellaneous other Green Building Costs 332
- 8.6 Design and Analysis Tools and Methods 336

9

UNDERSTANDING SPECIFICATIONS

- 9.1 General Overview 343
- 9.2 The Need for Specifications 345
- 9.3 Specifications Categories 348
- 9.4 The Project Manual 351
- 9.5 Specification Formation and Organization 361
- 9.6 Computerized Specification Writing Systems 372
- 9.7 Liability Concerns 376

10

LITIGATION AND LIABILITY ISSUES

- 10.1 General Overview 378
- 10.2 Liability Issues 382
- 10.3 Responsibility for Failure, Negligence, and Standard of Care 385
- 10.4 Traditional Litigation Versus Alternative Dispute Resolution 392
- 10.5 Insurance Needs 399

11

GREEN PROJECT COMMISSIONING

- 11.1 General Overview 411
- 11.2 Commissioning Objectives and Goals 414
- 11.3 Planning the Commissioning Process 419
- 11.4 Commissioning Authority 423
- 11.5 The Commissioning Process 427

12

GREEN BUSINESS DEVELOPMENT

- 12.1 General 439
 - 12.2 The Office: Home Based or Bricks-and-Mortar? 440
 - 12.3 Creating a Business Plan 441
 - 12.4 Startup Costs, Setting a Budget, and Capitalization 444
 - 12.5 Creating a Corporate Image 450
 - 12.6 Identifying and Tracking Sources for Leads 453
 - 12.7 Selling Yourself 453
 - 12.8 Business Forms, Licenses, Permits, and Insurance 460
 - 12.9 Taxes Strategies and Incentives 466
 - 12.10 The Bidding Process and Types of Building Contracts 467
 - 12.11 Creating a Website and Internet Marketing 473
- Appendix One Acronyms & Abbreviations 485
- Appendix Two Glossary 496
- Bibliography 520
- Index 525
